


PROJET RIAD90.mpp

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	November		April		September		February		July		December		May		October	
								E	B	M	E	B	M	E	B	M	E	B	M	E	B	M	E
1		ETAPE FUSION	90 days	Thu 01/01/15	Wed 06/05/15																		
2		ATELIER FONDERIE	90 days	Thu 01/01/15	Wed 06/05/15		fondeuse[20%];agents[40%]																
3		ETAPE PRIPARATION	150 days	Sat 25/04/15	Thu 19/11/15																		
4		ATELIER OXYDE	50 days	Thu 07/05/15	Wed 15/07/15	2	agents[3%];machine[6]																
5		ATELIER MALAXAGE	100 days	Thu 11/06/15	Wed 28/10/15	4	agents[3%];machine[6]																
6		ETAPE COUPE ET FINITION	396 days	Sat 05/09/15	Fri 10/03/17																		
7		ATELIER EMPATTAGE	90 days	Thu 29/10/15	Wed 02/03/16	5	machine[12];agents[12%]																
8		ATELIER SECHAGE	90 days	Sun 06/03/16	Thu 07/07/16	7	machine[12];agents[24%]																
9		ATELIER COUPNE	108 days	Fri 08/07/16	Tue 06/12/16	8	machine[8];agents[8%]																
10		ENVELOPPEUSE	108 days	Thu 21/07/16	Mon 19/12/16	9FS-012 days	machine[6];agents[2%]																
11		ETAPE MONTER	126 days	Thu 01/12/16	Thu 25/05/17																		
12		ATELIER C.O.S	18 days	Tue 20/12/16	Thu 12/01/17	01	machine[1];agents[12%]																
13		ATELIER MONTAGE	108 days	Mon 13/03/17	Wed 09/08/17	21FS-06 days	machine[6];agents[12%]																
14		ETAPE TEST	153 days	Thu 01/06/17	Mon 01/01/18																		
15		ATELIER FORMATION	150 days	Tue 06/06/17	Mon 01/01/18	31FS-06 days	machine[6];agents[48%]																

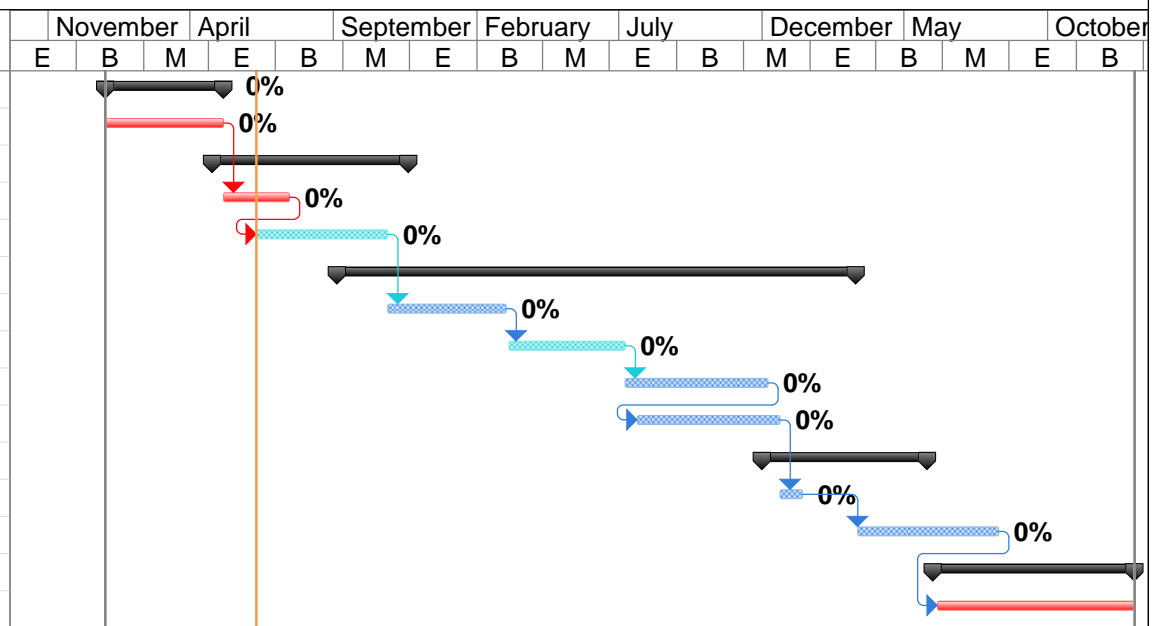

Critical		Task Progress		Baseline		Summary		Inactive Task	
Critical Split		Manual Task		Baseline Split		Manual Summary		Inactive Milestone	
Critical Progress		Start-only		Baseline Milestone		Project Summary		Inactive Summary	
Task		Finish-only		Milestone		External Tasks		Deadline	
Split		Duration-only		Summary Progress		External Milestone			
